


Access Compliance Report Public Rights-of-Way (Curb Ramps)



Intersection ID: 26999Main Street:SETON_HOUSE_LNCross Street:SHEPHERDLEAS_LNLocation:NEADA ID: 0C0A9C61FF11Ramp Type:PerpDiagInitial Pass/Fail:FailOverall Compliance:NoSeverity Score:8.75

Codes/Mitigation Info/Possible Solution

Field Measurements/Component Compliance

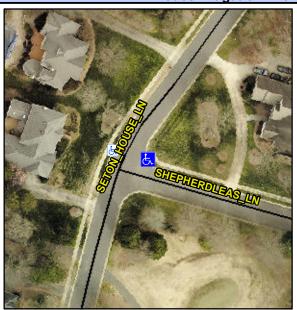

Street 1 Name
Stop Condition-Street 2
Street 2 Name
Stop Condition-Street 1

SETON HOUSE LN None SHEPHERLEAS LN StopSign Possible Solutions:

Remove & Replace Curb Ramp With
Two New Directional Ramps or
Equivalent.

Surveyor Notes:

N/A

PROW/ADA:

R304.5.1

Total Cost: \$ 3200.00

| Field Measurements/Component Compliance | | | | | |
|---|--|------|------|-----------------------------|------|
| Compliance Description | | Data | Comp | liance Description | Data |
| N/A | Ramp Length (in) | 49.0 | Yes | Ramp Slope (%) | 6.4 |
| No | Ramp Width (in) | 36.5 | Yes | Ramp XSlope (%) | 0.7 |
| N/A | Flare Type LT | N/A | N/A | Flare Type RT | N/A |
| N/A | Flare Slope LT (%) | N/A | N/A | Flare Slope RT (%) | N/A |
| N/A | Flare Traversable LT? | N/A | N/A | Flare Traversable RT? | N/A |
| N/A | Landing Length (in) | N/A | N/A | DWS Provided? | N/A |
| N/A | Landing Width (in) | N/A | N/A | DWS Contrast? | N/A |
| N/A | Landing Slope (%) | N/A | N/A | DWS Length (in) | N/A |
| N/A | Landing X Slope (%) | N/A | N/A | DWS Full Width? | N/A |
| N/A | Landing Curb? (Y/N) | N/A | N/A | DWS Offset (in) | N/A |
| N/A | Shared Landing? | N/A | | | |
| N/A | Gutter Ponding? | N/A | N/A | Gutter Slope (%) | N/A |
| N/A | Gutter Lip Ht (in) | N/A | N/A | Gutter X Slope (%) | N/A |
| N/A | Painted X Walk1? | No | N/A | Painted X Walk2? | No |
| | X Walk 1 Direction | To W | | X Walk 2 Direction | To S |
| N/A | X Walk 1 Width (in) | N/A | N/A | X Walk 2 Width (in) | N/A |
| | X Walk 1 Slope (%) | 7.8 | | X Walk 2 Slope (%) | 5.5 |
| | X Walk 1 X Slope (%) | 2.2 | | X Walk 2 X Slope (%) | 6.7 |
| N/A | Ramp inside XWalk1? | N/A | N/A | Ramp inside XWalk2? | N/A |
| | Road Slope (%) | 0.8 | N/A | Clear Space? | N/A |
| | Road X Slope (%) | 9.1 | N/A | Clear Space to XWalk (in) | N/A |
| N/A | Any Obstructions? | N/A | N/A | Storm Grate/Utility Hazard? | N/A |
| | Obstruction Type | | | Storm Grate/Utility Type | |
| | | N/A | | | N/A |
| | | | Yes | Surface Condition? (G/P) | Good |
| | A CONTRACTOR OF THE CONTRACTOR | | | | |





