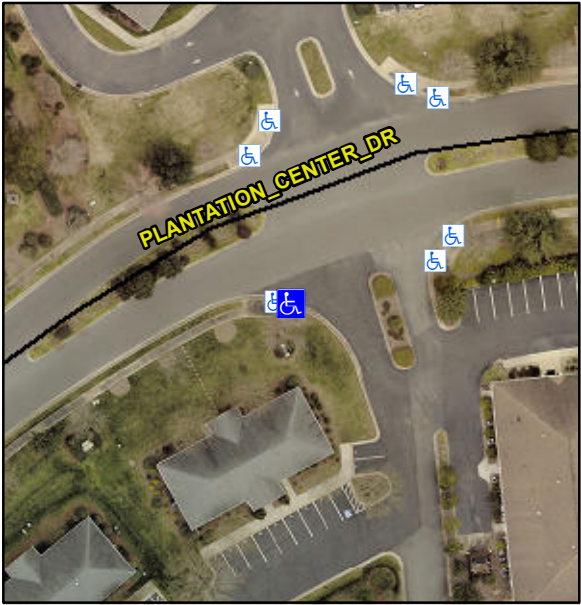


Access Compliance Report

Public Rights-of-Way

(Curb Ramps)

| | | | |
|---------------------------|-----------------------------------|-------------------------|------------------------|
| Intersection ID: 10034609 | Main Street: PLANTATION_CENTER_DR | Cross Street: N/A | Location: SW |
| ADA ID: 1579A30AA59B | Ramp Type: Para | Initial Pass/Fail: Fail | Overall Compliance: No |
| | | | Severity Score: 13.75 |

| Codes/Mitigation Info/Possible Solution | | | Field Measurements/Component Compliance | | |
|---|--|--|---|-----------------------------|--------------|
|  | Possible Solutions: | | Compliance | Description | Data |
| | Remove & Replace Entire Ramp. | | N/A | Ramp Length LT (in) | 54.0 |
| | | | Yes | Ramp Width LT (in) | 108.0 |
| | | | No | Ramp Slope LT (%) | 8.9 |
| | | | Yes | Ramp XSlope LT (%) | 1.8 |
| | | | N/A | Landing Length (in) | N/A |
| | | | N/A | Landing Width (in) | N/A |
| | | | N/A | Landing Slope (%) | N/A |
| | | | N/A | Landing X Slope (%) | N/A |
| | | | N/A | Landing Curb? (Y/N) | N/A |
| <p>Surveyor Notes:</p> <p>N/A</p> <p>PROW/ADA:</p> <p>R304.3.2, R304.5.3</p> | | | N/A | Ramp XSlope RT (%) | 5.4 |
| | | | No | Ramp XSlope RT (%) | 3.7 |
| | | | N/A | DWS Provided? | N/A |
| | | | N/A | DWS Contrast? | N/A |
| | | | N/A | DWS Length (in) | N/A |
| | | | N/A | DWS Full Width? | N/A |
| | | | N/A | DWS Offset (in) | N/A |
| | | | N/A | Gutter Slope (%) | N/A |
| | | | N/A | Gutter X Slope (%) | N/A |
| | | | N/A | Painted X Walk1? | No |
| <p>Street 1 Name</p> <p>Stop Condition-Street 1</p> <p>Street 2 Name</p> <p>Stop Condition-Street 2</p> | | | To NE | X Walk 2 Direction | N/A |
| | | | N/A | X Walk 2 Width (in) | N/A |
| | | | 0.2 | X Walk 2 Slope (%) | N/A |
| | | | 3.7 | X Walk 2 X Slope (%) | N/A |
| | | | N/A | Ramp inside XWalk2? | N/A |
| | | | N/A | Clear Space? | N/A |
| | | | N/A | Clear Space to XWalk (in) | N/A |
| | | | N/A | Storm Grate/Utility Hazard? | N/A |
| | | | | Storm Grate/Utility Type | |
| | | | N/A | Surface Condition? (G/P) | Good |
| Total Cost: | | | \$ | 1600.00 | 9.8 |

