

Access Compliance Report Public Rights-of-Way (Curb Ramps)




Intersection ID: 50232 Main Street: MARVIN_RD Cross Street: LONGSTONE_LN Location: W

ADA ID: 8E30B2F65710 Ramp Type: Perpendicular Diagonal Initial Pass/Fail: Pass Overall Compliance: No Severity Score: 0.25

Codes/Mitigation Info/Possible Solution

Field Measurements/Component Compliance

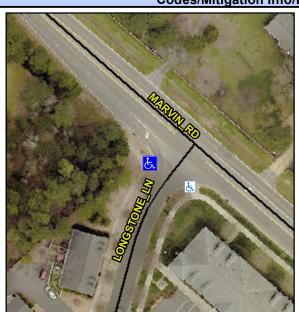

Street 1 Name
Stop Condition-Street 2
Street 2 Name
Stop Condition-Street 1

LONGSTONE LN StopSign MARVIN RD None Possible Solutions:

Remove & Replace Curb Ramp With Two New Directional Ramps or Equivalent.

Surveyor Notes:

N/A

PROW/ADA:

Not Found, R304.5.3, R305.2

Total Cost: \$ 3200.00

Field Measurements/Component Compilance					
Compliance Description		Data	Compliance Description		Data
N/A	Ramp Length (in)	83.0	Yes	Ramp Slope (%)	7.2
Yes	Ramp Width (in)	48.0	No	Ramp XSlope (%)	2.8
N/A	Flare Type LT	Sloped	N/A	Flare Type RT	N/A
N/A	Flare Slope LT (%)	10.0	Yes	Flare Slope RT (%)	0.9
N/A	Flare Traversable LT?	Yes	N/A	Flare Traversable RT?	Yes
Yes	Landing Length (in)	72.0	Yes	DWS Provided?	Yes
Yes	Landing Width (in)	48.0	Yes	DWS Contrast?	Yes
Yes	Landing Slope (%)	1.4	Yes	DWS Length (in)	24.0
No	Landing X Slope (%)	5.8	Yes	DWS Full Width?	Yes
N/A	Landing Curb? (Y/N)	No	No	DWS Offset (in)	3.5
N/A	Shared Landing?	No			
Yes	Gutter Ponding?	No	Yes	Gutter Slope (%)	3.0
Yes	Gutter Lip Ht (in)	0.0	Yes	Gutter X Slope (%)	1.5
N/A	Painted X Walk1?	No	N/A	Painted X Walk2?	No
	X Walk 1 Direction	To SE		X Walk 2 Direction	To NE
N/A	X Walk 1 Width (in)	N/A	N/A	X Walk 2 Width (in)	N/A
	X Walk 1 Slope (%)	0.4		X Walk 2 Slope (%)	2.3
	X Walk 1 X Slope (%)	2.4		X Walk 2 X Slope (%)	0.0
N/A	Ramp inside XWalk1?	N/A	N/A	Ramp inside XWalk2?	N/A
	Road Slope (%)	2.6	N/A	Clear Space?	Yes
	Road X Slope (%)	3.2	N/A	Clear Space to XWalk (in)	N/A
Yes	Any Obstructions?	No	Yes	Storm Grate/Utility Hazard?	No
	Obstruction Type			Storm Grate/Utility Type	
		N/A			N/A
			Yes	Surface Condition? (G/P)	Good





