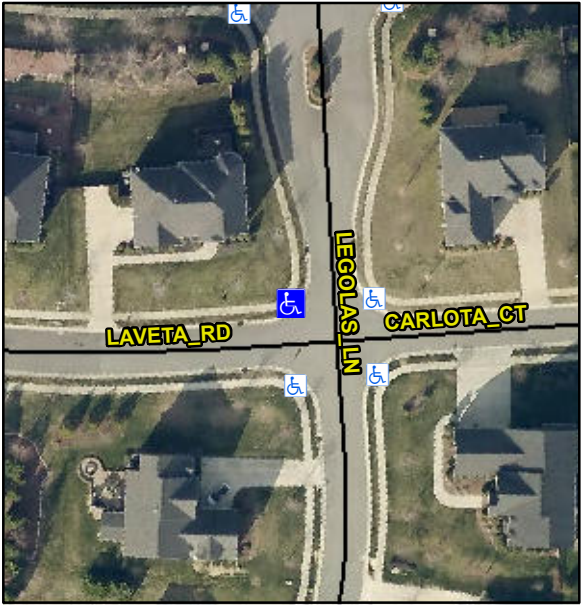


Access Compliance Report

Public Rights-of-Way

(Curb Ramps)

| | | | |
|------------------------|-------------------------|--------------------------|------------------------|
| Intersection ID: 49126 | Main Street: CARLOTA_CT | Cross Street: LEGOLAS_LN | Location: NW |
| ADA ID: A99DCC64462E | Ramp Type: PerpDiag | Initial Pass/Fail: Fail | Overall Compliance: No |
| | | Severity Score: 8.75 | |

| Codes/Mitigation Info/Possible Solution | | | Field Measurements/Component Compliance | | |
|---|---|------------|---|-----------------------------|-------------|
|  | Possible Solutions: | | Compliance | Description | Data |
| | Remove & Replace Curb Ramp With Two New Directional Ramps or Equivalent. | | Yes | Ramp Length (in) | 47.0 |
| | | | No | Ramp Width (in) | 41.0 |
| | | | N/A | Flare Type LT | N/A |
| | | | N/A | Flare Slope LT (%) | N/A |
| | | | N/A | Flare Traversable LT? | N/A |
| | | | N/A | Landing Length (in) | N/A |
| | | | N/A | Landing Width (in) | N/A |
| | | | N/A | Landing Slope (%) | N/A |
| | | | N/A | Landing X Slope (%) | N/A |
| | | | N/A | Landing Curb? (Y/N) | N/A |
| | | | N/A | Shared Landing? | N/A |
| | | | N/A | Gutter Ponding? | N/A |
| | | | N/A | Gutter Lip Ht (in) | N/A |
| | | | No | Painted X Walk1? | N/A |
| | | | To S | X Walk 1 Direction | N/A |
| | | | N/A | X Walk 1 Width (in) | N/A |
| | | | 0.1 | X Walk 1 Slope (%) | N/A |
| | | | 0.2 | X Walk 1 X Slope (%) | N/A |
| | | | N/A | Ramp inside XWalk1? | N/A |
| <p>Surveyor Notes:</p> <p>N/A</p> <p>PROW/ADA:</p> <p>Not Found, R304.5.1</p> | | | N/A | Flare Type RT | N/A |
| | | | N/A | Flare Slope RT (%) | N/A |
| | | | N/A | Flare Traversable RT? | N/A |
| | | | N/A | DWS Provided? | N/A |
| | | | N/A | DWS Contrast? | N/A |
| | | | N/A | DWS Length (in) | N/A |
| | | | N/A | DWS Full Width? | N/A |
| | | | N/A | DWS Offset (in) | N/A |
| | | | N/A | Gutter Slope (%) | N/A |
| | | | N/A | Gutter X Slope (%) | N/A |
| | | | No | Painted X Walk2? | N/A |
| | | | To E | X Walk 2 Direction | N/A |
| | | | N/A | X Walk 2 Width (in) | N/A |
| | | | 2.5 | X Walk 2 Slope (%) | N/A |
| | | | 0.5 | X Walk 2 X Slope (%) | N/A |
| | | | N/A | Ramp inside XWalk2? | N/A |
| | | | N/A | Clear Space? | N/A |
| | | | N/A | Clear Space to XWalk (in) | N/A |
| | | | N/A | Storm Grate/Utility Hazard? | N/A |
| | | | N/A | Storm Grate/Utility Type | N/A |
| | | | N/A | Surface Condition? (G/P) | Good |
| Total Cost: | | \$ 3200.00 | | | |

| | |
|-------------------------|------------|
| Street 1 Name | CARLOTA CT |
| Stop Condition-Street 2 | StopSign |
| Street 2 Name | LEGOLAS LN |
| Stop Condition-Street 1 | None |

