


# Access Compliance Report

## Public Rights-of-Way

### (Curb Ramps)

|   |                           |   |                        |
|---|---------------------------|---|------------------------|
| Intersection ID: 6218                   | Main Street: BEAM_LAKE_DR | Cross Street: PEACHWOOD_DR              | Location: SW           |
| ADA ID: F82CEBAFC3E7                    | Ramp Type: PerpDiag       | Initial Pass/Fail: Fail                 | Overall Compliance: No |
| Codes/Mitigation Info/Possible Solution |                           | Field Measurements/Component Compliance |                        |
| Severity Score: 36.25                   |                           |   |                        |

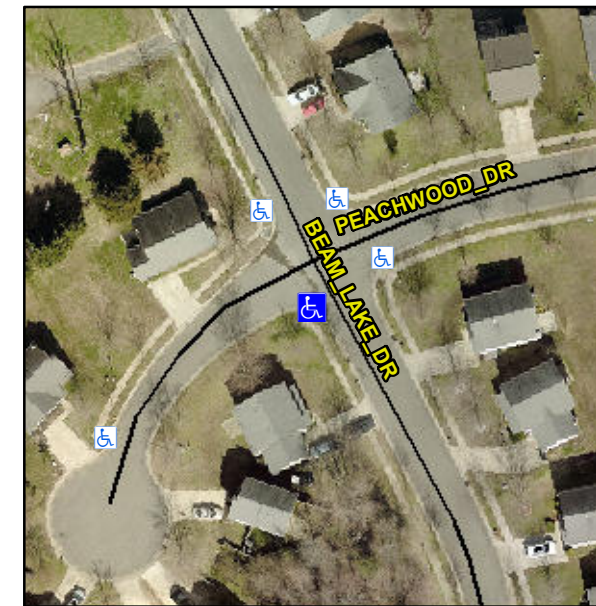

Possible Solutions:

**Remove & Replace Curb Ramp With Two New Directional Ramps or Equivalent.**

Surveyor Notes:

**N/A**

PROW/ADA:

**Not Found, R304.5.1, R304.5.3**

Total Cost: \$ 3200.00

| Compliance | Description           | Data  | Compliance | Description                 | Data  |
|------------|-----------------------|-------|------------|-----------------------------|-------|
| N/A        | Ramp Length (in)      | 47.0  | Yes        | Ramp Slope (%)              | 7.4   |
| No         | Ramp Width (in)       | 26.0  | No         | Ramp XSlope (%)             | 3.0   |
| N/A        | Flare Type LT         | N/A   | N/A        | Flare Type RT               | N/A   |
| N/A        | Flare Slope LT (%)    | N/A   | N/A        | Flare Slope RT (%)          | N/A   |
| N/A        | Flare Traversable LT? | N/A   | N/A        | Flare Traversable RT?       | N/A   |
| N/A        | Landing Length (in)   | N/A   | N/A        | DWS Provided?               | N/A   |
| N/A        | Landing Width (in)    | N/A   | N/A        | DWS Contrast?               | N/A   |
| N/A        | Landing Slope (%)     | N/A   | N/A        | DWS Length (in)             | N/A   |
| N/A        | Landing X Slope (%)   | N/A   | N/A        | DWS Full Width?             | N/A   |
| N/A        | Landing Curb? (Y/N)   | N/A   | N/A        | DWS Offset (in)             | N/A   |
| N/A        | Shared Landing?       | N/A   |            |                             |       |
| N/A        | Gutter Ponding?       | N/A   | N/A        | Gutter Slope (%)            | N/A   |
| N/A        | Gutter Lip Ht (in)    | N/A   | N/A        | Gutter X Slope (%)          | N/A   |
| N/A        | Painted X Walk1?      | No    | N/A        | Painted X Walk2?            | No    |
|            | X Walk 1 Direction    | To NE |            | X Walk 2 Direction          | To NW |
| N/A        | X Walk 1 Width (in)   | N/A   | N/A        | X Walk 2 Width (in)         | N/A   |
|            | X Walk 1 Slope (%)    | 3.9   |            | X Walk 2 Slope (%)          | 3.1   |
|            | X Walk 1 X Slope (%)  | 1.5   |            | X Walk 2 X Slope (%)        | 3.7   |
| N/A        | Ramp inside XWalk1?   | N/A   | N/A        | Ramp inside XWalk2?         | N/A   |
|            | Road Slope (%)        | 2.6   | N/A        | Clear Space?                | N/A   |
|            | Road X Slope (%)      | 1.3   | N/A        | Clear Space to XWalk (in)   | N/A   |
| N/A        | Any Obstructions?     | N/A   | N/A        | Storm Grate/Utility Hazard? | N/A   |
|            | Obstruction Type      |       |            | Storm Grate/Utility Type    |       |
|            |                       | N/A   |            |                             | N/A   |
|            |                       | Yes   |            | Surface Condition? (G/P)    | Good  |

Street 1 Name **BEAM LAKE DR**  
 Stop Condition-Street 2 **None**  
 Street 2 Name **PEACHWOOD DR**  
 Stop Condition-Street 1 **StopSign**

