


Access Compliance Report

Public Rights-of-Way

(Curb Ramps)

| | | | |
|---|---------------------------|---|------------------------|
| Intersection ID: 18627 | Main Street: CEDARBARK_DR | Cross Street: CLIFTON_MEADOW_DR | Location: E |
| ADA ID: 515772A2373E | Ramp Type: PerpDiag | Initial Pass/Fail: Fail | Overall Compliance: No |
| Codes/Mitigation Info/Possible Solution | | Field Measurements/Component Compliance | |
| Severity Score: 13.75 | | | |

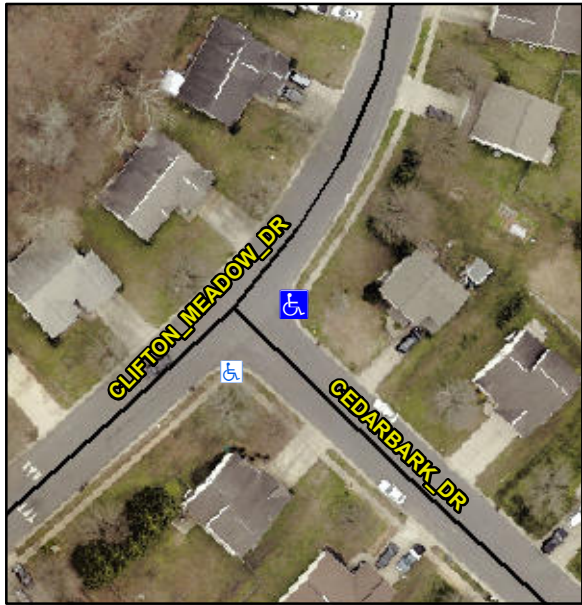

Street 1 NameCEDAR BARK DR

Stop Condition-Street 2None

Street 2 NameCLIFTON MEADOW DR

Stop Condition-Street 1StopSign

Possible Solutions:
Remove & Replace Curb Ramp With Two New Directional Ramps or Equivalent.

Surveyor Notes:
N/A

PROW/ADA:
R304.2.2, R304.5.3

Total Cost:\$3200.00

| Compliance | Description | Data | Compliance | Description | Data |
|------------|-----------------------|-------|------------|-----------------------------|-------|
| N/A | Ramp Length (in) | 37.0 | No | Ramp Slope (%) | 9.7 |
| Yes | Ramp Width (in) | 48.0 | No | Ramp XSlope (%) | 4.0 |
| N/A | Flare Type LT | N/A | N/A | Flare Type RT | N/A |
| N/A | Flare Slope LT (%) | N/A | N/A | Flare Slope RT (%) | N/A |
| N/A | Flare Traversable LT? | N/A | N/A | Flare Traversable RT? | N/A |
| N/A | Landing Length (in) | N/A | N/A | DWS Provided? | N/A |
| N/A | Landing Width (in) | N/A | N/A | DWS Contrast? | N/A |
| N/A | Landing Slope (%) | N/A | N/A | DWS Length (in) | N/A |
| N/A | Landing X Slope (%) | N/A | N/A | DWS Full Width? | N/A |
| N/A | Landing Curb? (Y/N) | N/A | N/A | DWS Offset (in) | N/A |
| N/A | Shared Landing? | N/A | | | |
| N/A | Gutter Ponding? | N/A | N/A | Gutter Slope (%) | N/A |
| N/A | Gutter Lip Ht (in) | N/A | N/A | Gutter X Slope (%) | N/A |
| N/A | Painted X Walk1? | No | N/A | Painted X Walk2? | No |
| | X Walk 1 Direction | To NW | | X Walk 2 Direction | To SW |
| N/A | X Walk 1 Width (in) | N/A | N/A | X Walk 2 Width (in) | N/A |
| | X Walk 1 Slope (%) | 5.3 | | X Walk 2 Slope (%) | 1.9 |
| | X Walk 1 X Slope (%) | 0.2 | | X Walk 2 X Slope (%) | 0.6 |
| N/A | Ramp inside XWalk1? | N/A | N/A | Ramp inside XWalk2? | N/A |
| | Road Slope (%) | 1.2 | N/A | Clear Space? | N/A |
| | Road X Slope (%) | 1.7 | N/A | Clear Space to XWalk (in) | N/A |
| N/A | Any Obstructions? | N/A | N/A | Storm Grate/Utility Hazard? | N/A |
| | Obstruction Type | | | Storm Grate/Utility Type | |
| | | N/A | | | N/A |
| | | | Yes | Surface Condition? (G/P) | Good |

Total Cost: \$ 3200.00

