Access Compliance Report
Public Rights-of-Way
(Curb Ramps)

Intersection ID: 46187 **Main Street:** YAUPON_RD **Cross Street:** FERNSPRAY_RD **Location:** NE

ADA ID: 13C5D4E1A1EB **Ramp Type:** PerpDiag **Initial Pass/Fail:** Pass **Overall Compliance:** No **Severity Score:** 0

Codes/Mitigation Info/Possible Solution

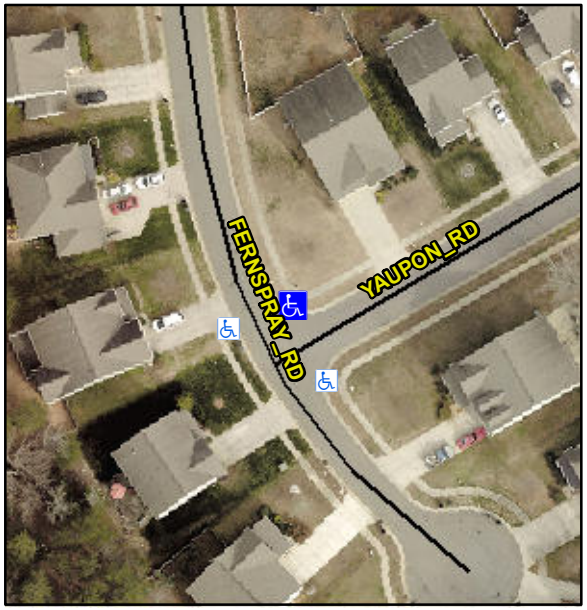

Possible Solutions:

Remove & Replace Curb Ramp With Two New Directional Ramps or Equivalent. Remove & Replace Gutter.

Surveyor Notes:

N/A

PROW/ADA:

R304.2.1, R305.2, R304.5.3

Street 1 Name	FERNSPRAY RD
Stop Condition-Street 2	None
Street 2 Name	YAUPON RD
Stop Condition-Street 1	StopSign

Total Cost: $ 3950.00

Field Measurements/Component Compliance

Compliance	Description	Data	Compliance	Description	Data
N/A	Ramp Length (in)	72.5	Yes	Ramp Slope (%)	6.1
Yes	Ramp Width (in)	48.0	Yes	Ramp XSlope (%)	0.8
N/A	Flare Type LT	Sloped	N/A	Flare Type RT	N/A
N/A	Flare Slope LT (%)	4.7	N/A	Flare Slope RT (%)	5.2
N/A	Flare Traversable LT?	No	N/A	Flare Traversable RT?	No
No	Landing Length (in)	46.0	Yes	DWS Provided?	Yes
Yes	Landing Width (in)	48.0	Yes	DWS Contrast?	Yes
Yes	Landing Slope (%)	0.8	Yes	DWS Length (in)	24.5
Yes	Landing X Slope (%)	0.7	Yes	DWS Full Width?	Yes
N/A	Landing Curb? (Y/N)	No	No	DWS Offset (in)	3.0
N/A	Shared Landing?	No			
Yes	Gutter Ponding?	No	Yes	Gutter Slope (%)	1.1
Yes	Gutter Lip Ht (in)	0.0	No	Gutter X Slope (%)	3.1
N/A	Painted X Walk1?	No	N/A	Painted X Walk2?	No
	X Walk 1 Direction	To W		X Walk 2 Direction	To S
N/A	X Walk 1 Width (in)	N/A	N/A	X Walk 2 Width (in)	N/A
	X Walk 1 Slope (%)	3.1		X Walk 2 Slope (%)	2.3
	X Walk 1 X Slope (%)	2.4		X Walk 2 X Slope (%)	4.4
N/A	Ramp inside XWalk1?	N/A	N/A	Ramp inside XWalk2?	N/A
	Road Slope (%)	1.6	N/A	Clear Space?	Yes
	Road X Slope (%)	3.9	N/A	Clear Space to XWalk (in)	N/A
Yes	Any Obstructions?	No	Yes	Storm Grate/Utility Hazard?	No
	Obstruction Type			Storm Grate/Utility Type	
		N/A			N/A
			Yes	Surface Condition? (G/P)	Good
